

FACT SHEET  
**Broward County, FL BEC**  
 Construction (C)  
 Congressional Districts: 20, 21, 22, 23, 25

### 1. DESCRIPTION

Broward County is located on the lower Atlantic Coast of Florida about 30 miles north of Miami. The project was authorized by the River and Harbor Act of 1965, Section 934 of the Water Resources Development Act (WRDA) of 1986 and in Section 506(a) WRDA 1996, which allows the Secretary to perform periodic beach nourishment for Segments II and III over a period of 50 years. Initial authorization provided for construction by the local sponsor with reimbursement of the Federal share of eligible costs. The City of Deerfield Beach is the Sponsor for initial construction of Segment I. Broward County is the sponsor for Segments II & III and has initially constructed and renourished the project since 1970.

### 2. FUNDING

|                         |                |
|-------------------------|----------------|
| Estimated Total Cost    | \$ 223,000,000 |
| Estimated Federal Cost  | \$125,400,000  |
| Allocation thru FY14    | \$46,217,238   |
| Allocation for FY15     | 0              |
| President's Budget FY16 | 0              |

### 3. SPONSORS

SEGMENT I – City of Deerfield Beach  
 150 N.E. Second Avenue  
 Deerfield Beach, FL 33441-8598

SEGMENTS II & III - Broward County Board of Commissioners  
 218 SW First Avenue  
 Ft. Lauderdale, FL 33301

### 4. STATUS


**SEG I** - The Sponsor provided funds in FY 2008 for the U.S. Army Corps of Engineers (Corps) to initiate Engineering and Design (E&D) for preparation of a General Reevaluation Report (GRR) for initial construction. Completion of the GRR was scheduled in FY 2013, contingent upon the sponsor providing additional funds to continue the preparation of the GRR. This work effort has been on hold since FY 2011 due to lack of Sponsor funds.

**SEG II** – The County intends to construct the second (and last) renourishment event of Segment II in 2015 within the limits of the authorized project. A Limited Reevaluation Report (LRR) has been prepared by the Sponsor to document changes in borrow sources, provide updated costs, verify the continued economic justification and environmental acceptability of the authorized project and support execution of a Project Partnership Agreement. To accompany the LRR, an Environmental Assessment (EA) has been prepared to document the new borrow sources. The final report has been completed and is currently under Agency Technical Review before submitting to SAD for approval.

**SEG III** – A reimbursement, over \$18.3M, was provided to Sponsor (owed to since 2007) as part of the Federal share of Broward County Seg III 2nd Renourishment. Sponsor has planned next renourishment of Seg III in 2018. Efforts for an LRR for the 3<sup>rd</sup> renourishment of Seg III will be initiated in FY15.

**POST-SANDY EFFORTS** – Construction of the Segment II FCCE project was completed on schedule in February 2014, ahead of schedule. Over 135K cubic yards of beach fill material was placed along 5.2 miles of shoreline above mean high water via truck haul operation. Post construction environmental and physical monitoring currently underway.

# Broward County

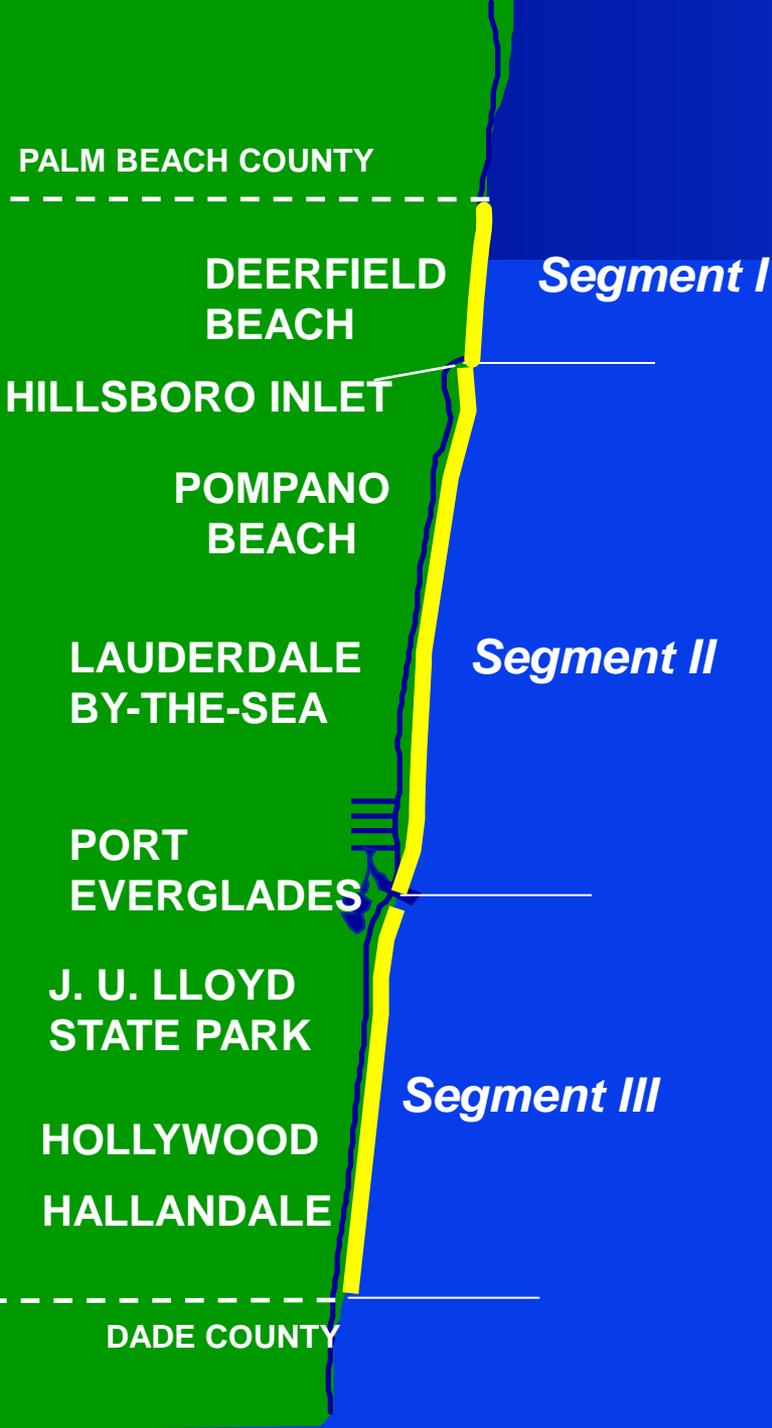

**Segments I, II & III Shore Protection Project (SPP)**
