

FACT SHEET
Broward County, FL Shore Protection Project (SPP)
 Construction (C)
 Congressional Districts: 20, 21, 22, 23, 25

1. DESCRIPTION

Broward County is located on the lower Atlantic Coast of Florida about 30 miles north of Miami. The project was authorized by the River and Harbor Act of 1965, Section 934 of the Water Resources Development Act (WRDA) of 1986 and in Section 506(a) WRDA 1996, which allows the Secretary to perform periodic beach nourishment for Segments II and III over a period of 50 years. Initial authorization provided for construction by the local sponsor with reimbursement of the Federal share of eligible costs. The City of Deerfield Beach is the Sponsor for initial construction of Segment I. Broward County is the sponsor for Segments II & III and has initially constructed and renourished the project since 1970.

2. FUNDING

Estimated Total Cost	\$227,577,000
Estimated Federal Cost	\$127,885,000
Allocation thru FY15	\$66,646,000
Allocation for FY16	\$0
President's Budget FY17	\$0

3. SPONSORS

SEGMENT I – City of Deerfield Beach
 150 N.E. Second Avenue
 Deerfield Beach, FL 33441-8598

SEGMENTS II & III - Broward County Board of Commissioners
 218 SW First Avenue
 Ft. Lauderdale, FL 33301


4. STATUS

SEG I - The Sponsor provided funds in FY08 for the U.S. Army Corps of Engineers (Corps) to initiate Engineering and Design (E&D) for preparation of a General Reevaluation Report (GRR) for initial construction. Completion of the GRR was scheduled in FY13, contingent upon the sponsor providing additional funds to continue the preparation of the GRR. This work effort has been on hold since FY11 due to lack of Sponsor funds.

SEG II – The County is currently constructing the second (and last) renourishment event of Segment II within the limits of the authorized project and is scheduled to be complete in 2017. A Limited Reevaluation Report (LRR) was prepared by the Sponsor to document changes in borrow sources, provide updated costs, verify the continued economic justification and environmental acceptability of the authorized project. and was approved by USACE-HQ. To accompany the LRR, an Environmental Assessment (EA) has been prepared to document the new borrow sources. The Project Partnership Agreement for construction was executed on 24 November 2015.

SEG III – A reimbursement, over \$18.3 million, was provided to Sponsor (owed to since 2007) as part of the Federal share of Broward County Seg III 2nd Renourishment. Sponsor has planned next renourishment of Seg III in 2018. Efforts for an LRR for the 3rd renourishment of Seg III will be initiated in FY17.

Broward County

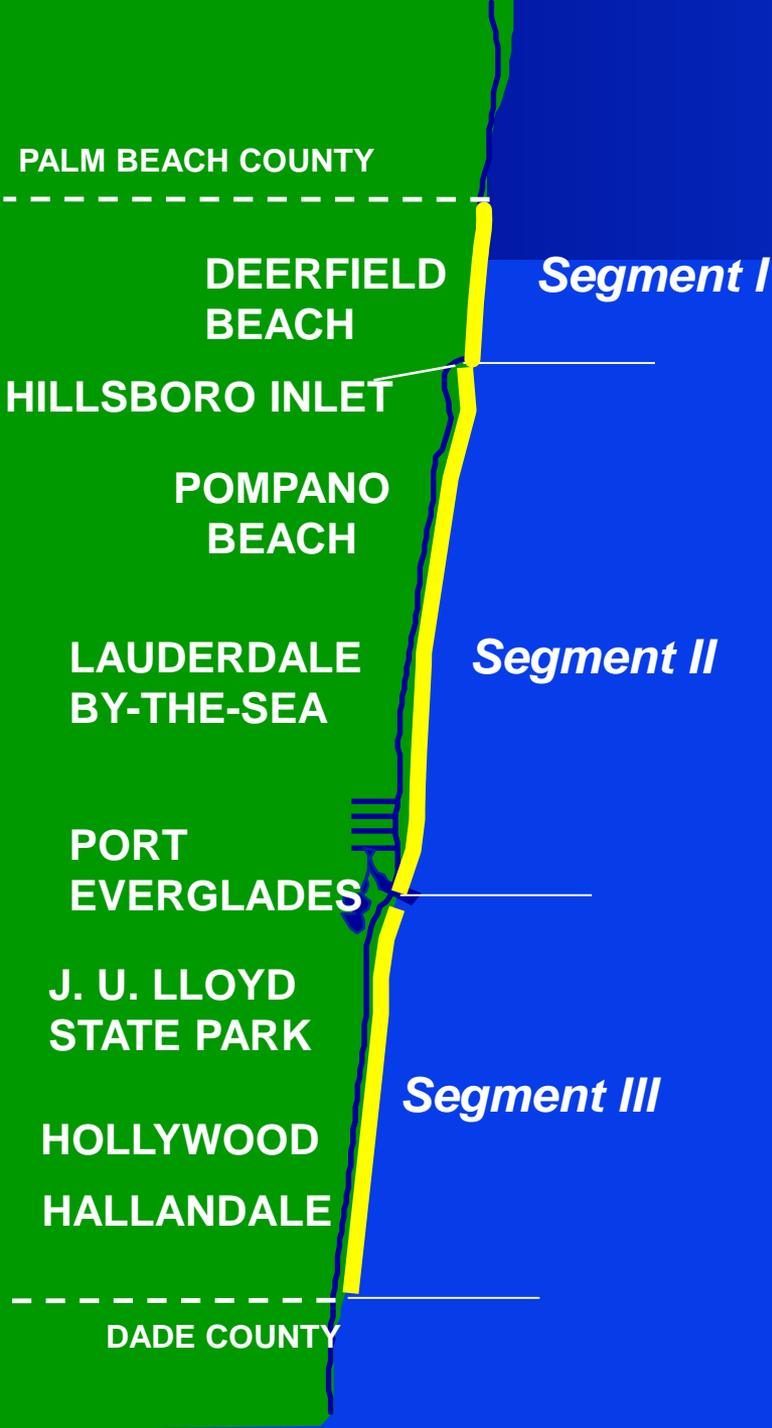

Segments I, II & III Shore Protection Project (SPP)
