
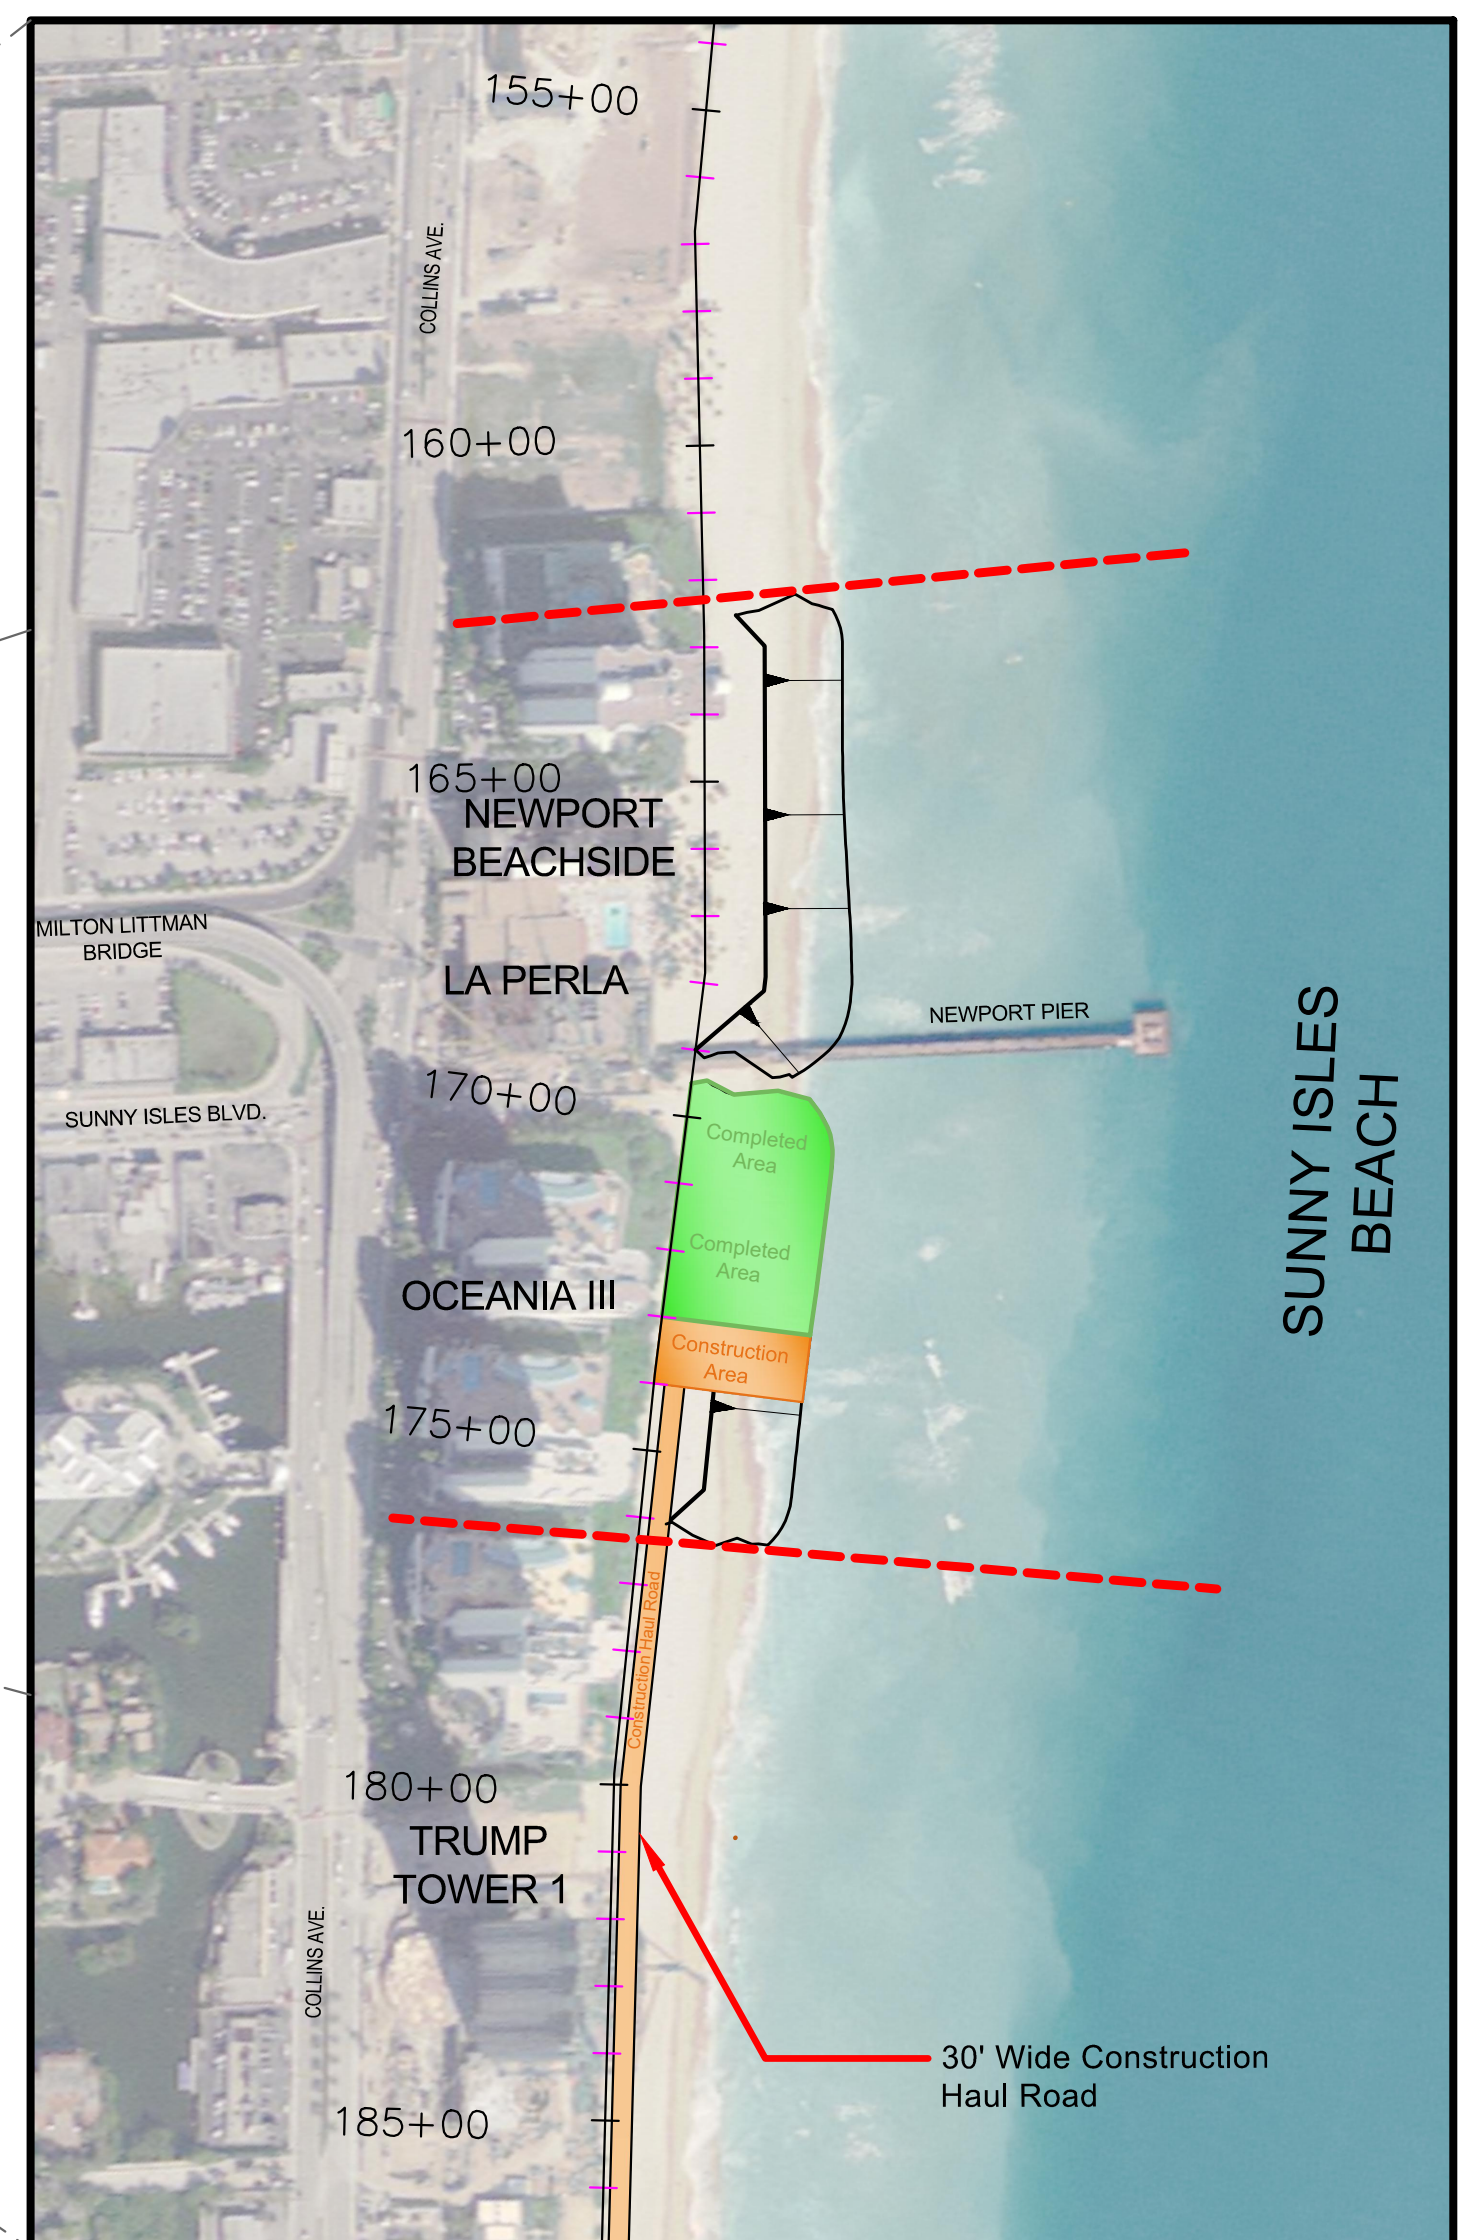
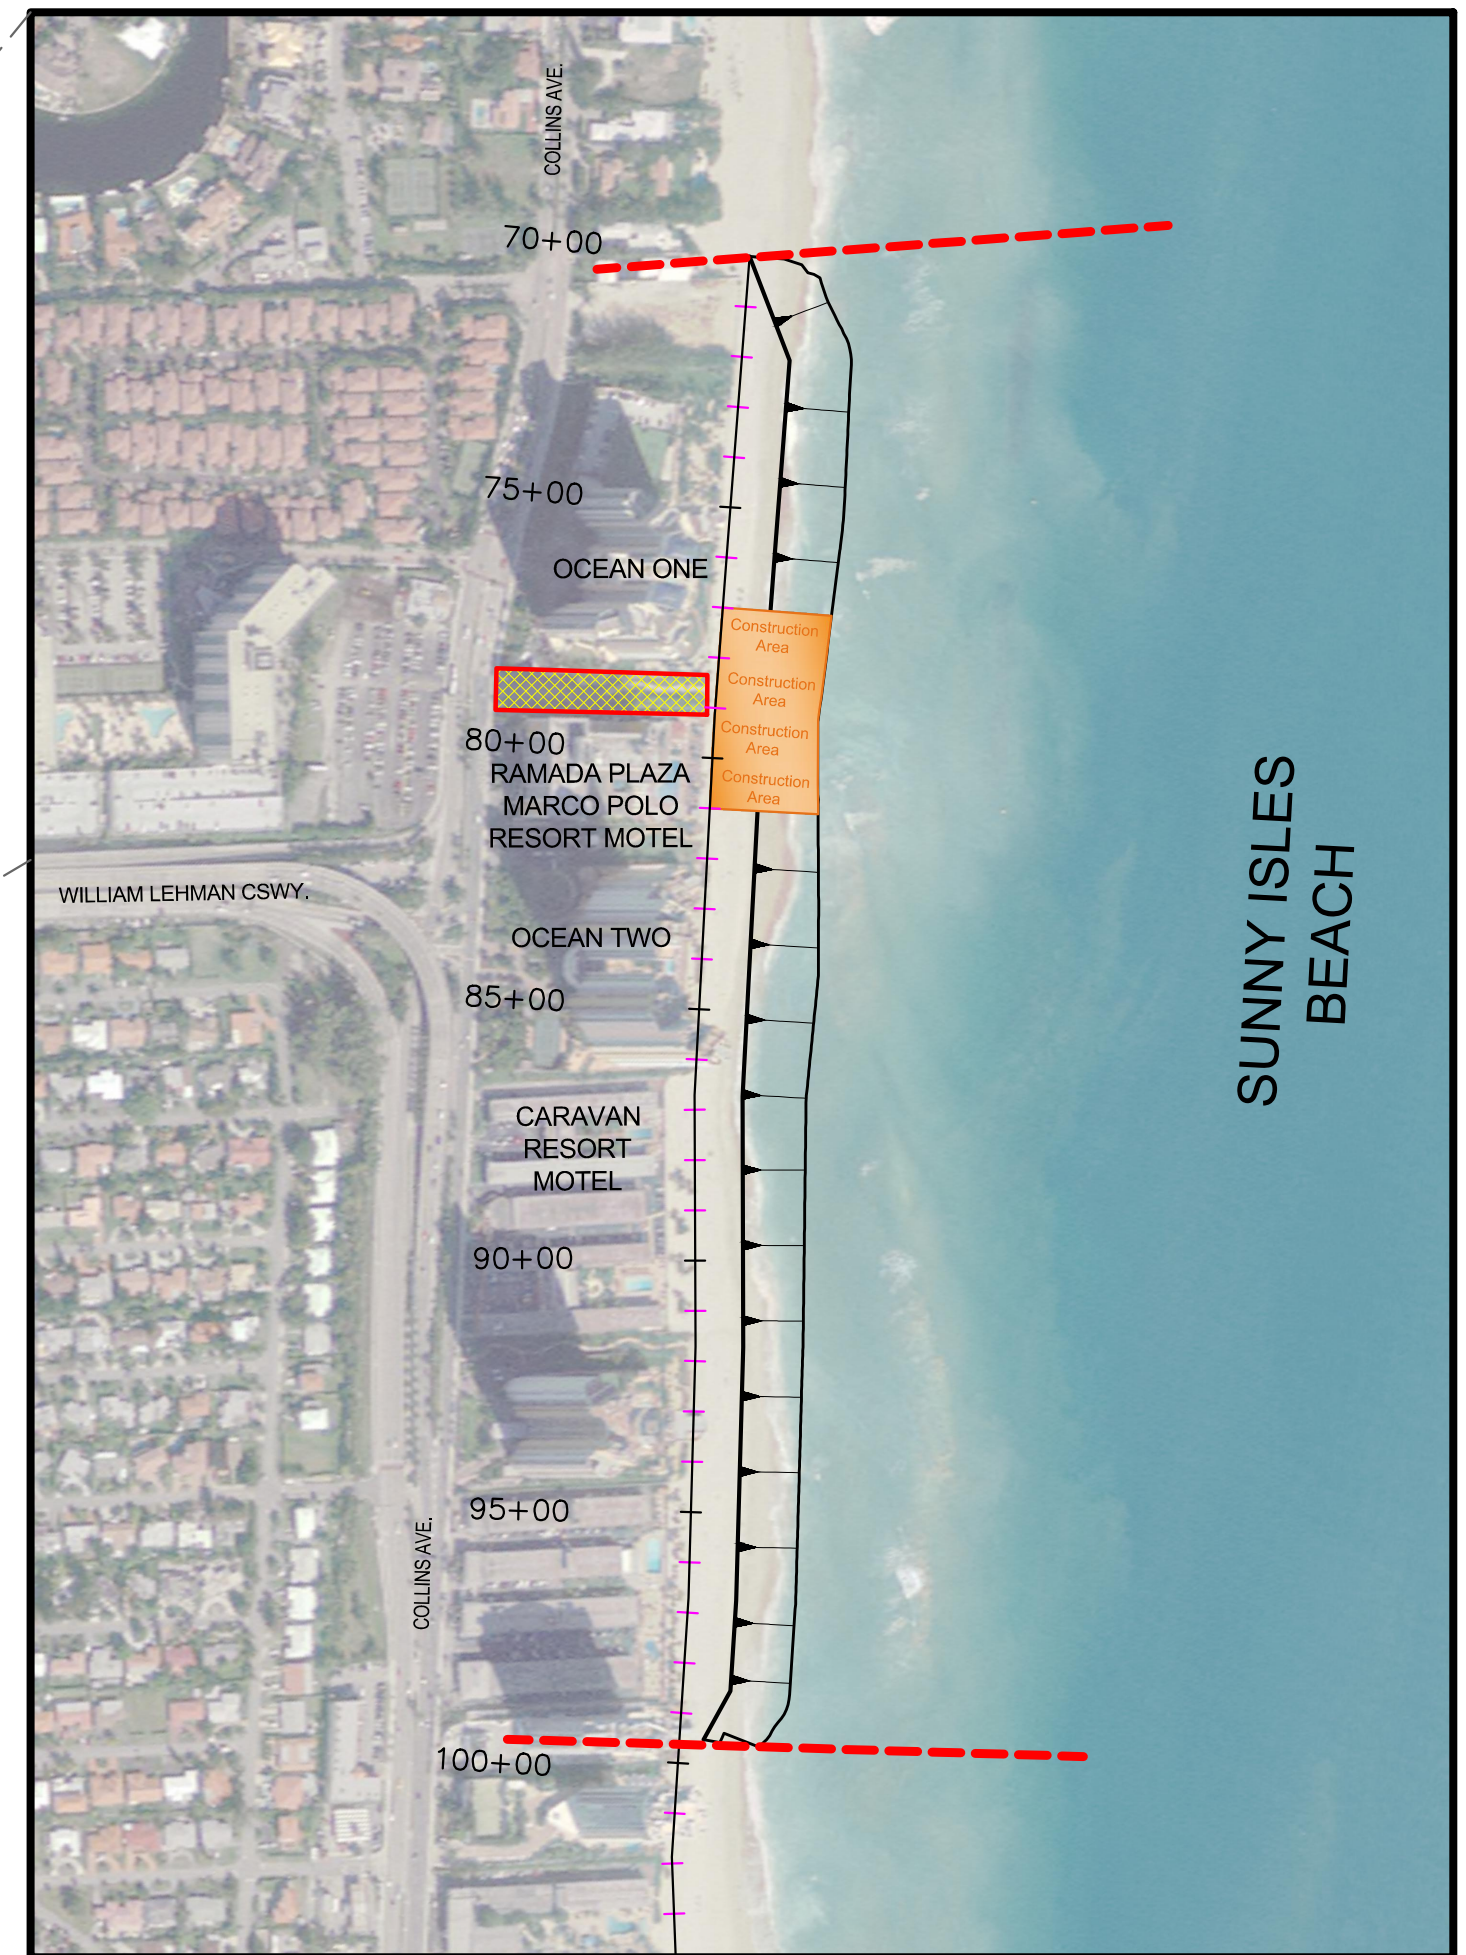


North Construction Access
(Ellen Wynne Beach Path)
Start Date: Nov. 9, 2017
End Date: March 30, 2018

Middle Construction Access
(Former Travel Lodge Motel)
Start Date: Nov. 13, 2017
End Date: Dec. 1, 2017

South Construction Access
(Haulover Park)
Start Date: Oct. 26, 2017
End Date: Dec. 1, 2017

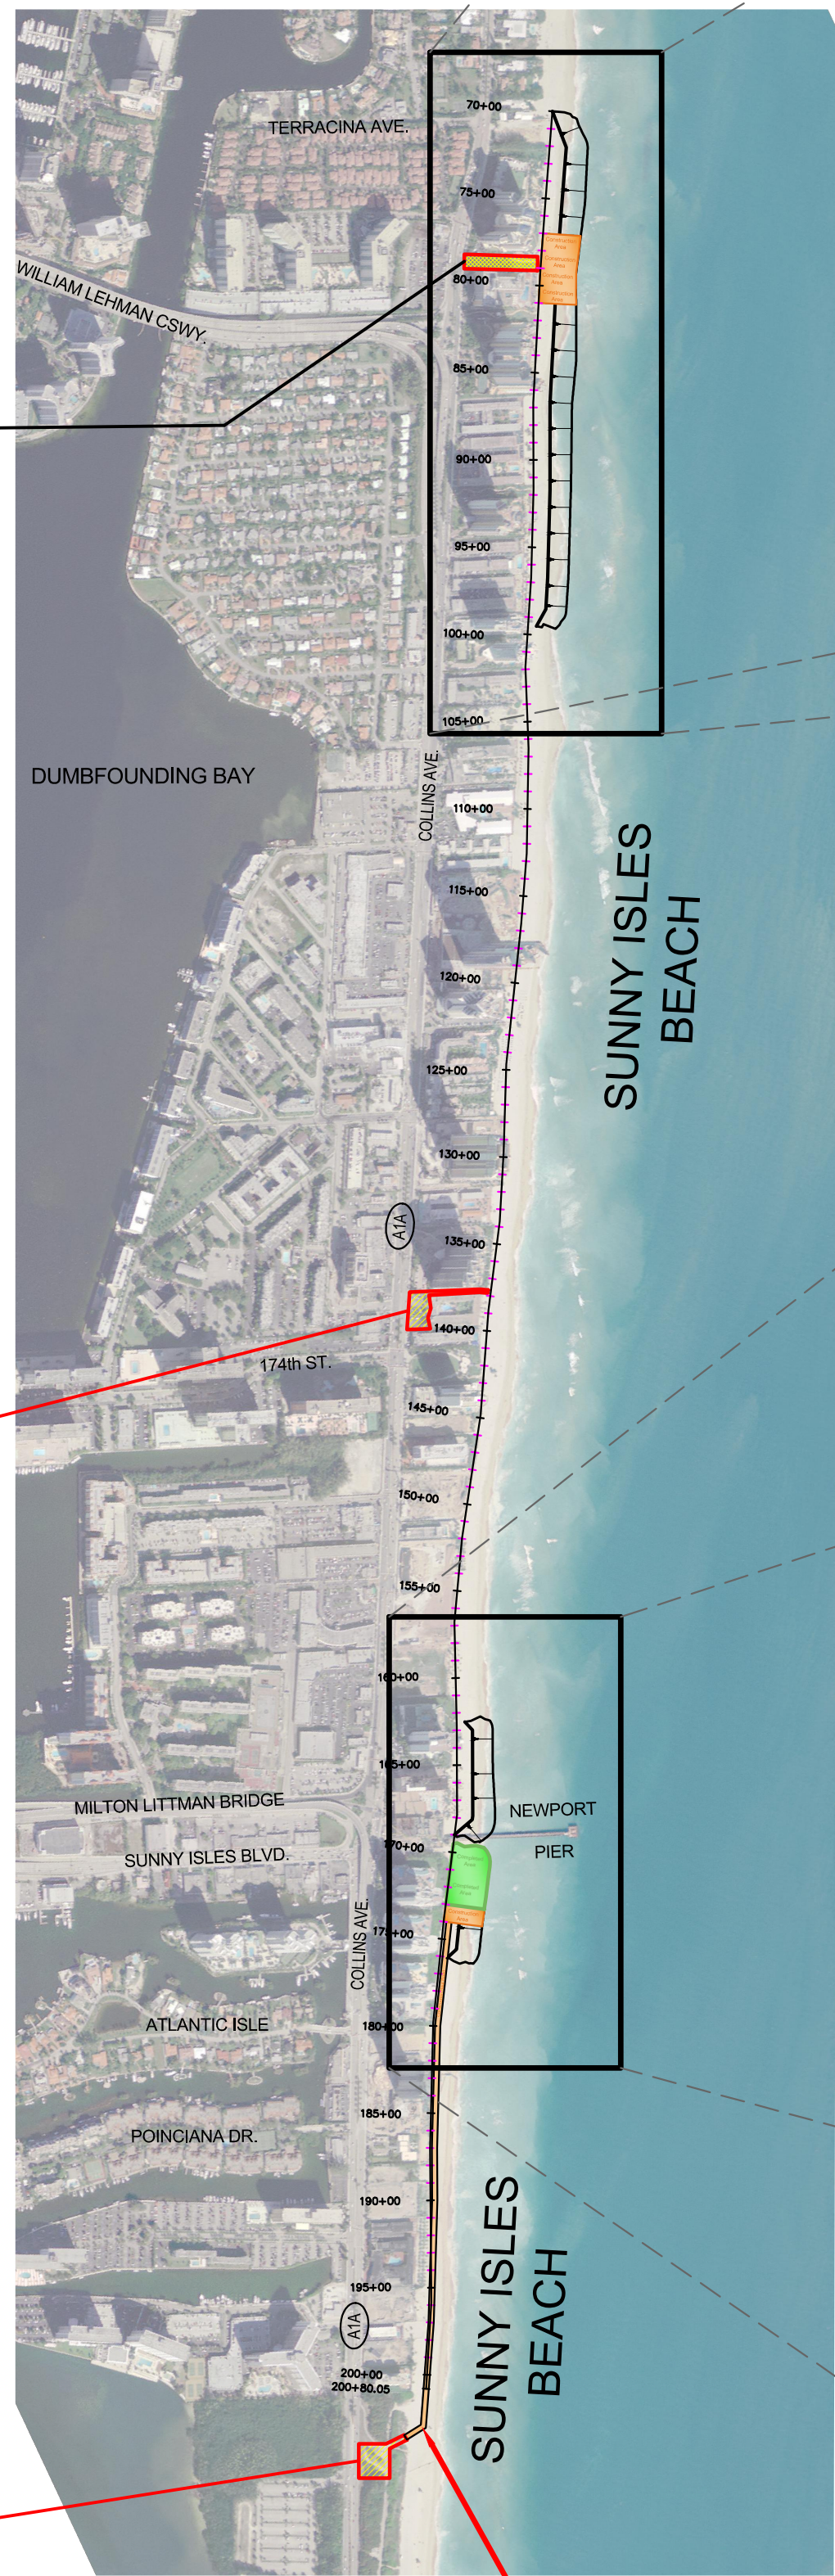

PROGRESS MAP OVERVIEW

Beach Erosion Control and Hurricane
Protection Project, Miami-Dade County,
Florida, Beach Renourishment 2017
Sunny Isles Beach

LEGEND:

	START/ END OF PROJECT
	MONUMENT/ SECTION LINES
	BEACH UNDER CONSTRUCTION
	COMPLETED BEACH CONSTRUCTION
	DESIGNATED ACCESS IN USE OR UNDER CONSTRUCTION



North Construction Access
(Ellen Wynne Beach Path)
Start Date: Nov. 9, 2017
End Date: March 30, 2018


Estimated Completion
Date: November 22, 2017

LEGEND:

	START/ END OF PROJECT
	MONUMENT/ SECTION LINES
	BEACH UNDER CONSTRUCTION
	COMPLETED BEACH CONSTRUCTION
	DESIGNATED ACCESS IN USE OR UNDER CONSTRUCTION

BASE BID
North Access (Ellen Wynne)
ZOOM-IN VIEW

Beach Erosion Control and Hurricane Protection Project, Miami-Dade County, Florida, Beach Renourishment 2017 Sunny Isles Beach

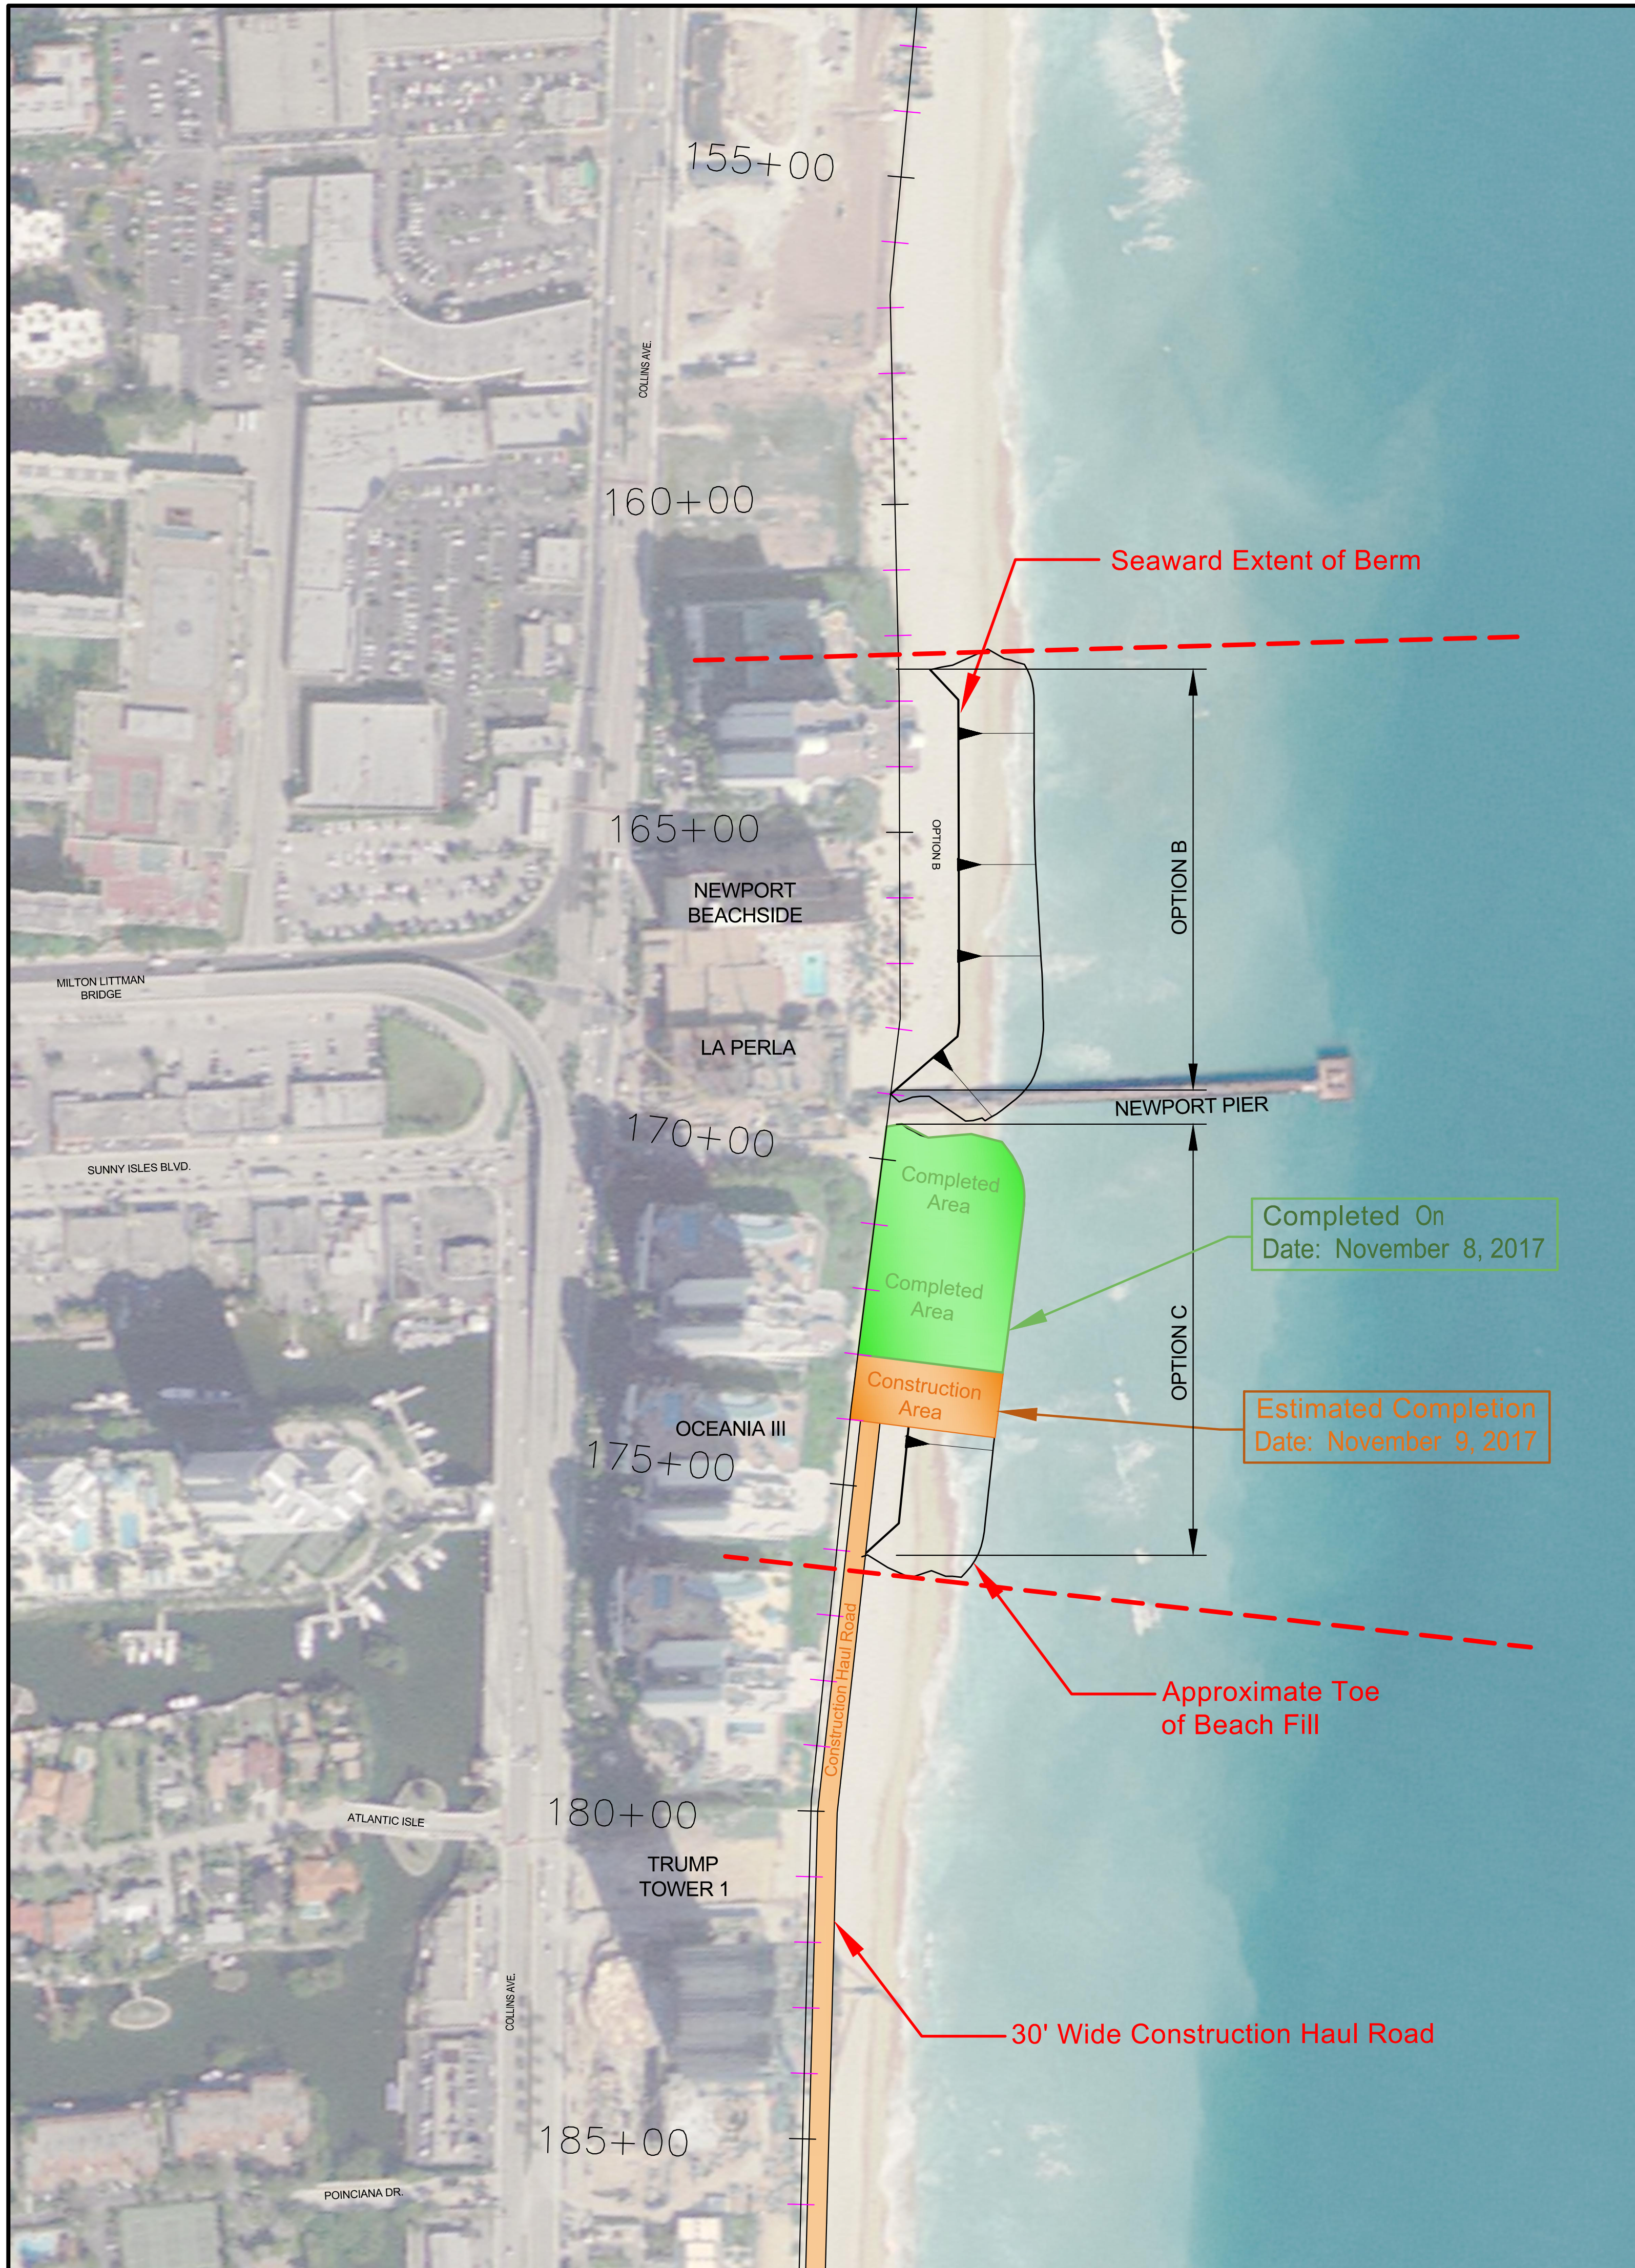

OPTIONS B & C

Middle Construction Access (Former Travel Lodge) and
South Construction Access (Haulover Park)

ZOOM-IN VIEW

Beach Erosion Control and Hurricane
Protection Project, Miami-Dade County,
Florida, Beach Renourishment 2017
Sunny Isles Beach

LEGEND:

	START/ END OF PROJECT
	SECTION LINES
	BEACH UNDER CONSTRUCTION
	COMPLETED BEACH CONSTRUCTION
	DESIGNATED ACCESS IN USE OR UNDER CONSTRUCTION
