

FACT SHEET
Jacksonville Harbor, FL
 Construction (C)
 Congressional Districts: 3, 4, 5

1. DESCRIPTION

Jacksonville Harbor is located in Duval County, Florida. The Harbor consists of 20 river miles starting at the mouth of the St. Johns River where it empties into the Atlantic Ocean. The study focuses on the portion of the harbor up to River Mile 20. The harbor project provides access to deep draft vessel traffic using terminal facilities located in the City of Jacksonville, Florida. The primary concentration of port facilities along Jacksonville Harbor is between miles 8 and 20 of the Federal navigation project. The recommended plan is the locally preferred plan (LPP), which includes deepening the Federal channel to 47 feet from the entrance channel to approximately River Mile 13; two areas of widening at the Training Wall Reach and St. Johns Bluff Reach; and two new turning basins at Blount Island and Brills Cut.

2. FUNDING

Estimated Total Cost	\$12,883,910 (GRR)
Estimated Federal Cost	\$8,426,517 (GRR)
Allocation thru FY15	\$8,426,517 (GRR)
Allocation thru FY15	\$5,400,000 (PED)
Allocation for FY16	\$0 (PED)
President's Budget FY17	\$0 (PED)

3. SPONSOR

Jacksonville Port Authority
 2831 Talleyrand Avenue
 Jacksonville, FL 32206-3496


4. STATUS

The project was officially authorized as part of WRRDA 2014 however no Federal construction funds have been appropriated thus far. The local sponsor has agreed to move forward with advanced funds to initiate construction.

The plans/specifications for the first contract (Contract A) are 95% complete. Other key activities include finalizing the FDEP permit, vertical coordination of the draft PPA and

assistance to the local sponsor for the purchase of approximately 620 acres of conservation lands.

FDEP NOI	19 February 2016
WQC Issued by FDEP	15 April 2016
Conservation Lands Purchased	31 March 2016
PPA Execution	June 2016
Advertisement	August 2016
Award Contract A	September 2016

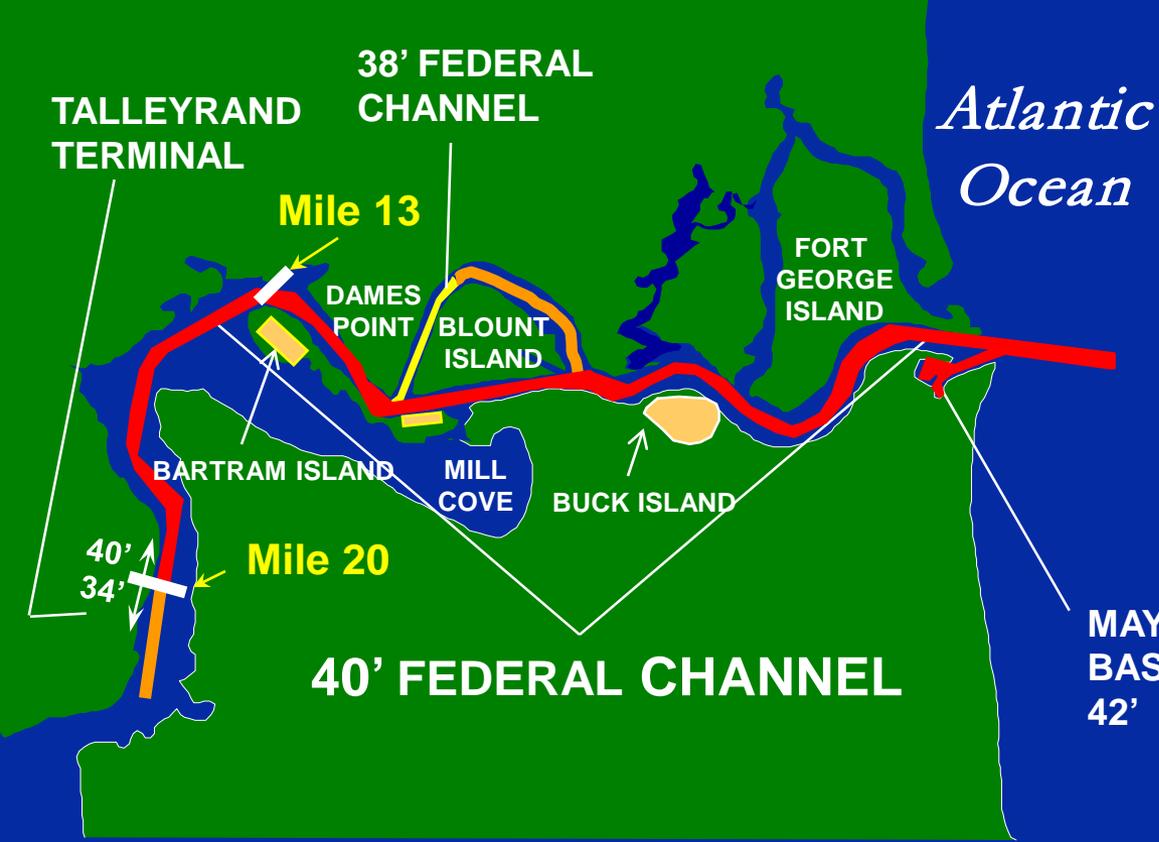

**JACKSONVILLE HARBOR,
FLORIDA**
